

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**



## South Street Paving Project & Water Main Replacement

[welcome](#)

---

[where are we now?](#)

---

[daily schedule](#)

---

[map](#)

---

[contacts](#)

---

[give'em a brake](#)


---





# welcome

home

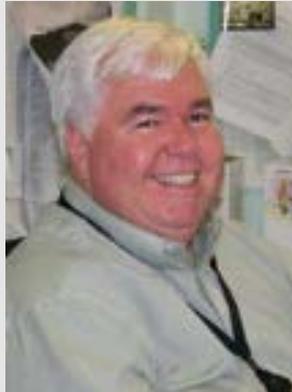

'Caring about city streets is caring about the People who use them. The purpose of this website is to keep the people of Auburn and the surrounding areas informed about the progress of the South Street water main installation and paving project.

We're all very excited to see this project underway. We recognize the people are share holders in this endeavor and our goal with this web page is to provide you with up to date information on the progress of the project. There will be inconvenience through the summer but we're sure you'll agree the work is needed. When the work is complete we'll have a highway that will do credit to our beloved national historic district.

We welcome any suggestions or comments on how we're doing.'

*William Lupien, Superintendent of Engineer Services*

welcome

---

where are we now?

---

daily schedule

---

map

---

contacts

---

give'em a brake

---

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**





# where are we now?

[home](#)



This July Rizzo Construction, Inc. from Auburn, NY along with C&S Companies, the engineers, from Syracuse, NY, will begin setting up shop on the project site.

We will begin work by installing a new 12" water main from Metcalf Drive to Lincoln Street. This work will take the better part of this construction season. At the same time we may also begin work on painting the street light posts, working on the pedestrian signals at the intersections and improve handicap access at intersections. At the completion of the water main work there will be a Winter shutdown

In 2015, after the winter shut down, the roadway part of the project will begin. We'll "mill" (remove old road surface) and in some limited areas remove the entire pavement. Manholes and drainage grates will be adjusted to match the new surface. We will then apply new blacktop. The plan requires two way traffic to be maintained at all times.

You will be able to check in weekly with "where are we now?" for a summary of what's been done, where we are now and what's planned for the future.

*Last updated July 31, 2014*

[welcome](#)

---

[where are we now?](#)

---

[daily schedule](#)

---

[map](#)

---

[contacts](#)

---

[give'em a brake](#)

---

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## Monday 07/28/14

### Metcalfe Drive to Chapman Avenue

- Laying out reference points on highway
- Saw cutting pavement in preparation for waterline excavation
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

Stay up to date on South Street construction progress online at:  
[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)






# map

home



Engineer's Field Office  
Lorraine Bldg

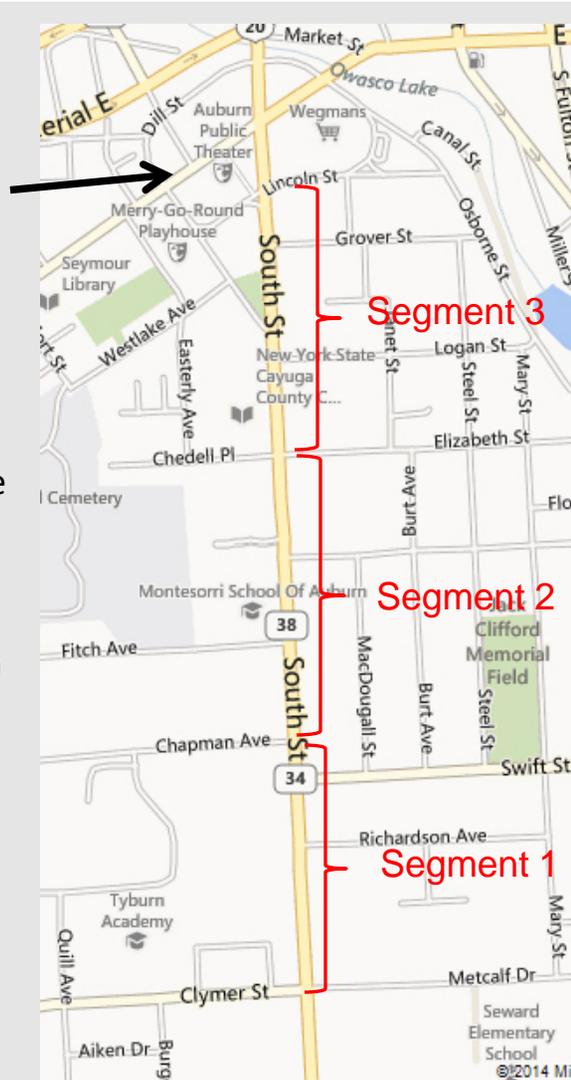

The work on the water main will proceed in three segments.

1. Metcalf Drive to Chapman Avenue
2. Chapman Ave to Elizabeth Street
3. Elizabeth Street to Lincoln Street

Paving of each segment will begin within five days of the completion of the water main installation for that segment.

The City, C&S Companies and Rizzo Constructions are all mindful of the historical importance of this area and its contributions to the character of Auburn.

welcome

---

where are we now?

---

daily schedule

---

map

---

contacts

---

give'em a brake

---

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**



Stay up to date on South Street construction progress online at:  
[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)



## contacts

[home](#)



**24 Hour Emergency**  
**Cellular (315)-277-0481**

### **ENGINEERS - C & S COMPANIES**

**Field Office** - Lorraine Building  
130 East Genesee Street.

**Resident Engineer** – Stephen Olschewske  
Office (315)-282-7336  
Cellular (315)-730-6479

### **CONTRACTOR – RIZZO CONSTRUCTION**

**Project Manager** – Kevin Rizzo  
Cellular (315)-406-1446

**Project Superintendent** - Bruce Corey  
Cellular (315)-277-0481

**Rizzo Construction**– Main Office  
Cellular (315)-252-1872

**City of Auburn – Engineering Services**  
(315)-255-4129

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)





# give'em a brake

home



Road crews who work in construction sites are part of families who need them, just like your family needs you. In the past five years, more than 11,000 people have been injured and more than 80 people have been killed in work zone crashes. This alarming statistic is punctuated by the fact that nearly all of those killed and injured were drivers or passengers traveling through work zones. With this in mind, it is important to drive with extra caution in work zones. Not just for the families who work in construction zones, but for your family too.

## Consider this

85% of those killed in work zones are drivers or passengers

Work zone fatalities occur every 7 hours—3 per day

Work zone injuries occur every 15 minutes—143 per day

welcome

---

where are we now?

---

daily schedule

---

map

---

contacts

---

give'em a brake

---

Stay up to date on South Street construction progress online at:  
[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## **Tuesday 07/29/14**

### **Metcalf Drive to Chapman Avenue**

- Laying out reference points on highway
- Saw cutting pavement in preparation for waterline excavation
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### **Chapman Avenue to Elizabeth Street**

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### **Elizabeth Street to Lincoln Street**

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**

[welcome](#)

---

[where are we now?](#)

---

[daily schedule](#)

---

[map](#)

---

[contacts](#)

---

[give'em a brake](#)

---





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## Wednesday 07/30/14

### Metcalfe Drive to Chapman Avenue

- Laying out reference points on highway
- Saw cutting pavement in preparation for waterline excavation
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

Stay up to date on South Street construction progress online at:  
[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## Thursday 07/31/14

### Metcalfe Drive to Chapman Avenue

- Laying out reference points on highway
- Saw cutting pavement in preparation for waterline excavation
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

Stay up to date on South Street construction progress online at:  
[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## **Friday 08/01/14**

### **Metcalf Drive to Chapman Avenue**

- Laying out reference points on highway
- Saw cutting pavement in preparation for waterline excavation
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### **Chapman Avenue to Elizabeth Street**

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

### **Elizabeth Street to Lincoln Street**

- Survey Crew marking out reference points
- Installing construction signs on South Street and side streets
- Materials deliveries at various off site locations

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## **Saturday 08/02/14**

### **Metcalfe Drive to Chapman Avenue**

- Contractor not working.

### **Chapman Avenue to Elizabeth Street**

- Contractor not working.

### **Elizabeth Street to Lincoln Street**

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**





# daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

## **Sunday 08/03/14**

### **Metcalfe Drive to Chapman Avenue**

- Contractor not working.

### **Chapman Avenue to Elizabeth Street**

- Contractor not working.

### **Elizabeth Street to Lincoln Street**

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**





Stay up to date on South Street construction progress online at:  
**[www.AuburnNY.gov/SouthStreet](http://www.AuburnNY.gov/SouthStreet)**
