



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



South Street Paving Project & Water Main Replacement

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)




Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



welcome

home

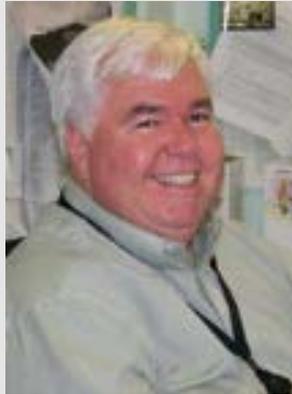

'Caring about city streets is caring about the People who use them. The purpose of this website is to keep the people of Auburn and the surrounding areas informed about the progress of the South Street water main installation and paving project.

We're all very excited to see this project underway. We recognize the people are share holders in this endeavor and our goal with this web page is to provide you with up to date information on the progress of the project. There will be inconvenience through the summer but we're sure you'll agree the work is needed. When the work is complete we'll have a highway that will do credit to our beloved national historic district.

We welcome any suggestions or comments on how we're doing.'

William Lupien, Superintendent of Engineer Services

welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



where are we now?

[home](#)



Work has begun!. You've probably noticed a lot of paint marks on the roadway. They let us know what's beneath the ground. In case you're wondering; Red = electric, Orange = communications, Blue = existing water, Green = sewer, Yellow = Gas, White = proposed excavation.

Saw cutting the pavement was the first order of business. That's done so when we begin the excavation for the new water main the edge of the trench will be neat and clean. That will allow us to pave up against a nice smooth edge.

You've also probably noticed a lot of black top batching. That's to provide a decent driving surface while the road is under construction. There will be times when traffic will be shifted from one side to another and we want your ride to be as good as possible under the circumstances.

The past week has been a lot preliminary work; this week will be the start of real construction. We realize that if we expect your patience we have to demonstrate a willingness to meet your needs. We will work with you to try and achieve that balance.

Last updated August 8, 2014

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Monday 08/11/14

Metcalfe Drive to Chapman Avenue

- Excavating and putting in new 12" water main.

Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Materials deliveries at various off site locations

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet




map

home



Engineer's
Field Office
Lorraine Bldg

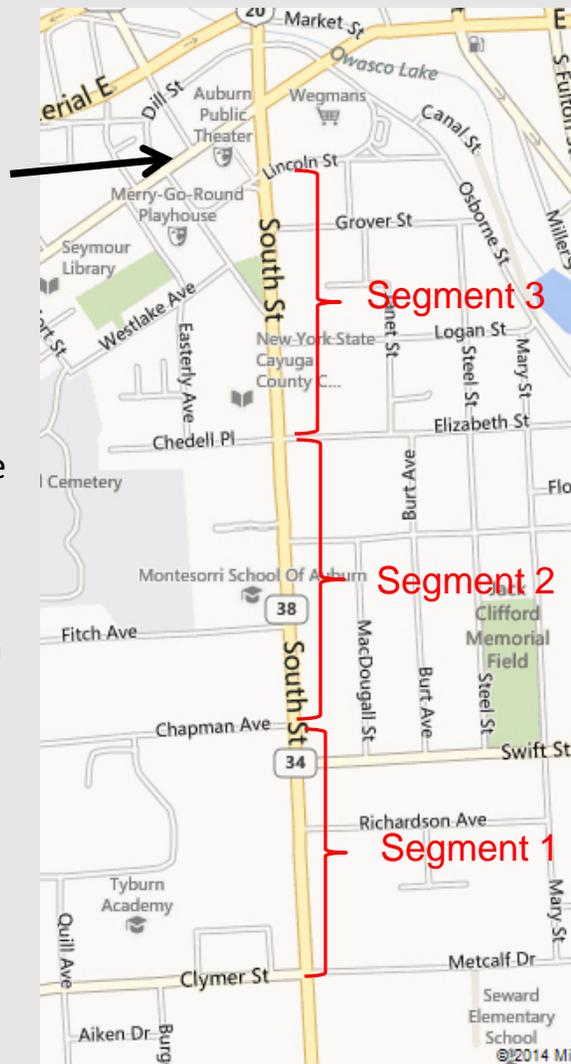

The work on the water main will proceed in three segments.

1. Metcalf Drive to Chapman Avenue
2. Chapman Ave to Elizabeth Street
3. Elizabeth Street to Lincoln Street

Paving of each segment will begin within five days of the completion of the water main installation for that segment.

The City, C&S Companies and Rizzo Construction are all mindful of the historical importance of this area and its contributions to the character of Auburn.

welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



contacts

[home](#)



24 Hour Emergency
Cellular (315)-277-0481

ENGINEERS - C & S COMPANIES

Field Office - Lorraine Building
130 East Genesee Street.

Resident Engineer – Stephen Olschewske
Office (315)-282-7336
Cellular (315)-730-6479

CONTRACTOR – RIZZO CONSTRUCTION

Project Manager – Kevin Rizzo
Cellular (315)-406-1446

Project Superintendent - Bruce Corey
Cellular (315)-277-0481

Rizzo Construction– Main Office
Cellular (315)-252-1872

City of Auburn – Engineering Services
(315)-255-4129

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



give'em a brake

[home](#)



Road crews who work in construction sites are part of families who need them, just like your family needs you. In the past five years, more than 11,000 people have been injured and more than 80 people have been killed in work zone crashes. This alarming statistic is punctuated by the fact that nearly all of those killed and injured were drivers or passengers traveling through work zones. With this in mind, it is important to drive with extra caution in work zones. Not just for the families who work in construction zones, but for your family too.

Consider this

85% of those killed in work zones are drivers or passengers

Work zone fatalities occur every 7 hours—3 per day

Work zone injuries occur every 15 minutes—143 per day

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Tuesday 08/12/14

Metcalfe Drive to Chapman Avenue

- Excavating and putting in new 12" water main.

Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Possibly some saw cutting of the pavement
- Materials deliveries at various off site locations

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Possibly install new sidewalk at the street corners.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Wednesday 08/13/14

Metcalfe Drive to Chapman Avenue

- Excavating and putting in new 12" water main.

Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Possibly some saw cutting of the pavement
- Materials deliveries at various off site locations

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Possibly install new sidewalk at the street corners.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Thursday 08/14/14

Metcalfe Drive to Chapman Avenue

- Excavating and putting in new 12" water main.

Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Possibly some saw cutting of the pavement
- Materials deliveries at various off site locations

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Possibly install new sidewalk at the street corners.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Friday 08/15/14

Metcalfe Drive to Chapman Avenue

- Excavating and putting in new 12" water main.

Chapman Avenue to Elizabeth Street

- Survey Crew marking out reference points
- Possibly some saw cutting of the pavement
- Materials deliveries at various off site locations

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Possibly install new sidewalk at the street corners.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Saturday 08/16/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Sunday 08/17/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet

