

Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



South Street Paving Project & Water Main Replacement

welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
welcome

home



'Caring about city streets is caring about the People who use them. The purpose of this website is to keep the people of Auburn and the surrounding areas informed about the progress of the South Street water main installation and paving project.

We're all very excited to see this project underway. We recognize the people are share holders in this endeavor and our goal with this web page is to provide you with up to date information on the progress of the project. There will be inconvenience through the summer but we're sure you'll agree the work is needed. When the work is complete we'll have a highway that will do credit to our beloved national historic district.

We welcome any suggestions or comments on how we're doing.'

William Lupien, Superintendent of Engineer Services



welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

where are we now?

[home](#)



Work on the water main continues at a very good pace and at this point is ahead of schedule. The water main from Metcalf Drive to Chapman has been pressure tested and disinfected. We will be hooking up the new water services in that section. The water main pipe from Chapman to Elizabeth Street has been installed and will soon be tested.

We are also progressing with blacktopping the trenches. We are placing 9 ½ inches of permanent blacktop in trenches. When that is done we will have completed work in the roadway for this season. Next season we will begin the paving of the roadway.

As stated, we will be installing new water services. You will be notified at least 24 hours prior any interruption to your water services. Businesses will be notified 48 hours in advance and where necessary we will make arrangements with businesses so as to not interrupt their services. Interruptions will normally be around 10 minutes.

Once again thank you for your patience.

Last updated September 5, 2014



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Monday 09/08/14 NO ROAD WORK

Metcalfe Drive to Chapman Avenue

- Placing Blacktop in water main trench.
- Installing new water services
- Clean up.

Chapman Avenue to Elizabeth Street

- Testing and disinfection of new water main and water main branches

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Begin placing water main pipe

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet




map

home



Engineer's
Field Office
Lorraine Bldg

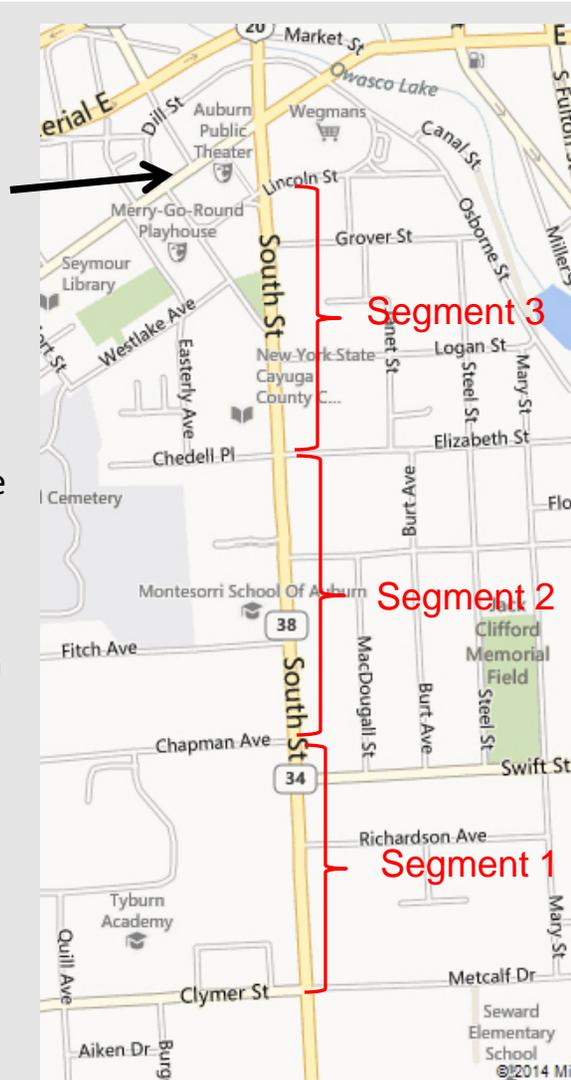

The work on the water main will proceed in three segments.

1. Metcalf Drive to Chapman Avenue
2. Chapman Ave to Elizabeth Street
3. Elizabeth Street to Lincoln Street

Paving of each segment will begin within five days of the completion of the water main installation for that segment.

The City, C&S Companies and Rizzo Construction are all mindful of the historical importance of this area and its contributions to the character of Auburn.

welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



contacts

[home](#)



24 Hour Emergency
Cellular 315-952-8963

ENGINEERS - C & S COMPANIES

Field Office - Lorraine Building
130 East Genesee Street.

Resident Engineer – Stephen Olschewske
Office (315)-282-7336
Cellular (315)-730-6479

CONTRACTOR – RIZZO CONSTRUCTION

Project Manager – Kevin Rizzo
Cellular (315)-406-1446

Project Superintendent - Bruce Corey
Cellular (315)-277-0481

Rizzo Construction– Main Office
Cellular (315)-252-1872

City of Auburn – Engineering Services
(315)-255-4129

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



give'em a brake

home



Road crews who work in construction sites are part of families who need them, just like your family needs you. In the past five years, more than 11,000 people have been injured and more than 80 people have been killed in work zone crashes. This alarming statistic is punctuated by the fact that nearly all of those killed and injured were drivers or passengers traveling through work zones. With this in mind, it is important to drive with extra caution in work zones. Not just for the families who work in construction zones, but for your family too.

Consider this

85% of those killed in work zones are drivers or passengers

Work zone fatalities occur every 7 hours—3 per day

Work zone injuries occur every 15 minutes—143 per day

welcome

where are we now?

daily schedule

map

contacts

give'em a brake



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Tuesday 09/09/14

Metcalfe Drive to Chapman Avenue

- Placing Blacktop in water main trench.
- Installing new water services
- Clean up.

Chapman Avenue to Elizabeth Street

- Testing and disinfection of new water main and water main branches

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Begin placing water main pipe

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Wednesday 09/10/14

Metcalfe Drive to Chapman Avenue

- Placing Blacktop in water main trench.
- Installing new water services
- Clean up.

Chapman Avenue to Elizabeth Street

- Testing and disinfection of new water main and water main branches

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Begin placing water main pipe

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Thursday 09/11/14

Metcalfe Drive to Chapman Avenue

- Placing Blacktop in water main trench.
- Installing new water services
- Clean up.

Chapman Avenue to Elizabeth Street

- Testing and disinfection of new water main and water main branches

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Begin placing water main pipe

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Friday 09/12/14

Metcalfe Drive to Chapman Avenue

- Placing Blacktop in water main trench.
- Installing new water services
- Clean up.

Chapman Avenue to Elizabeth Street

- Testing and disinfection of new water main and water main branches

Elizabeth Street to Lincoln Street

- Survey Crew marking out reference points
- Begin placing water main pipe

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Saturday 09/13/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Sunday 09/14/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet
