

Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



South Street Paving Project & Water Main Replacement

[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet

welcome

[home](#)



‘Caring about city streets is caring about the People who use them. The purpose of this website is to keep the people of Auburn and the surrounding areas informed about the progress of the South Street water main installation and paving project.

We’re all very excited to see this project underway. We recognize the people are share holders in this endeavor and our goal with this web page is to provide you with up to date information on the progress of the project. There will be inconvenience through the summer but we’re sure you’ll agree the work is needed. When the work is complete we’ll have a highway that will do credit to our beloved national historic district.

We welcome any suggestions or comments on how we’re doing.’

William Lupien, Superintendent of Engineer Services



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

where are we now?

[home](#)



Work on the water main is progressing ahead of schedule. We have currently stopped excavation at Grover Street so we can go back and start installing the water services for Section 2. We're also concentrating on placing blacktop in the pipe trenches.

The next and final stage of the water main work will resume from Grover Street to the Lincoln Street intersection soon. We need to do several "test pits" in the area to be certain of the location of under ground utilities. There is a heavy concentration of various utilities in this area; gas, electric, sewer, communications, etc. Although all these utilities have general locations, based on information provided by the different entities, we now need to get very exact information before proceeding with the new water main.

Digging trenches in the roadway is about as disruptive as it gets in highway construction. We are working very hard to get digging part of the work done, and it will be soon. We are moving as quickly as possible from Metcalf Drive toward the downtown area with our blacktopping and clean up. Thank you for your patience.

Last updated September 22, 2014



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

C&S
COMPANIES®

Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Monday 09/22/14

Metcalfe Drive to Chapman Avenue

- Clean up.

Chapman Avenue to Elizabeth Street

- Placing Blacktop in water main trench.
- Installing a few remaining new water services
- Hooking the water main into side street mains
- Clean up.

Elizabeth Street to Lincoln Street

- Digging test pits to determine exact location of utilities.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet



map

home




Engineer's
Field Office
Lorraine Bldg

The work on the water main will
proceed in three segments.

1. Metcalf Drive to Chapman Avenue
2. Chapman Ave to Elizabeth Street
3. Elizabeth Street to Lincoln Street

Paving of each segment will begin with
in five days of the completion of the
water main installation for that
segment.

The City, C&S Companies and Rizzo
Constructions are all mindful of the
historical importance of this area and
it's contributions to the character of
Auburn.

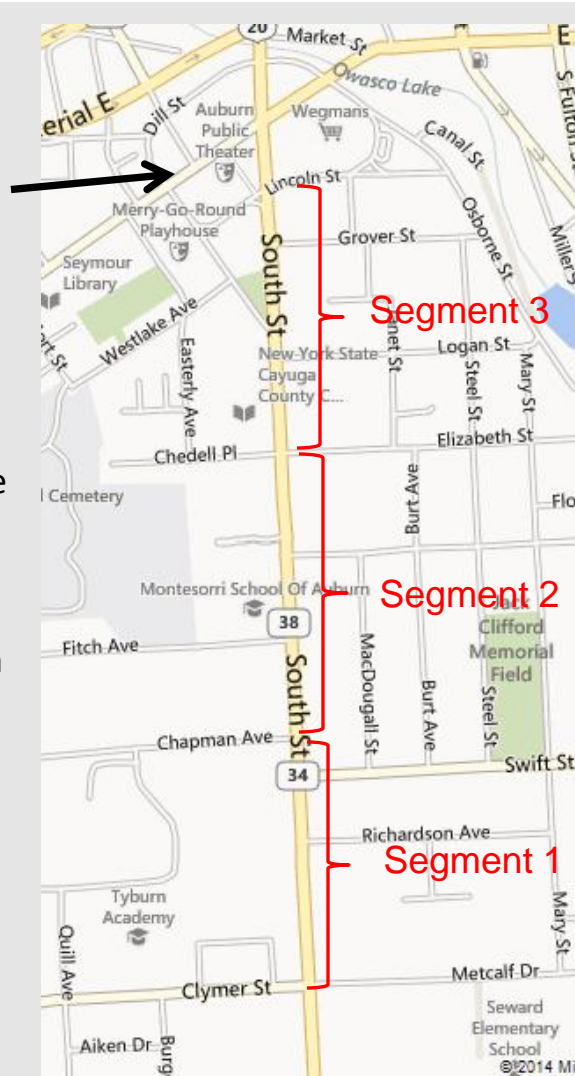

welcome

where are we now?

daily schedule

map

contacts

give'em a brake

C&S
COMPANIES®

Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet

contacts

[home](#)



24 Hour Emergency
Cellular 315-952-8963

ENGINEERS - C & S COMPANIES

Field Office - Lorraine Building
130 East Genesee Street.

Resident Engineer – Stephen Olschewske
Office (315)-282-7336
Cellular (315)-730-6479

CONTRACTOR – RIZZO CONSTRUCTION

Project Manager – Kevin Rizzo
Cellular (315)-406-1446

Project Superintendent - Bruce Corey
Cellular (315)-277-0481

Rizzo Construction– Main Office
Cellular (315)-252-1872

City of Auburn – Engineering Services
(315)-255-4129



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

give'em a brake

[home](#)



Road crews who work in construction sites are part of families who need them, just like your family needs you. In the past five years, more than 11,000 people have been injured and more than 80 people have been killed in work zone crashes. This alarming statistic is punctuated by the fact that nearly all of those killed and injured were drivers or passengers traveling through work zones. With this in mind, it is important to drive with extra caution in work zones. Not just for the families who work in construction zones, but for your family too.

Consider this

85% of those killed in work zones are drivers or passengers

Work zone fatalities occur every 7 hours—3 per day

Work zone injuries occur every 15 minutes—143 per day



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Tuesday 09/23/14

Metcalf Drive to Chapman Avenue

- Clean up.

Chapman Avenue to Elizabeth Street

- Placing Blacktop in water main trench.
- Installing a few remaining new water services
- Hooking the water main into side street mains
- Clean up.

Elizabeth Street to Lincoln Street

- Digging test pits to determine exact location of utilities.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Wednesday 09/24/14

Metcalf Drive to Chapman Avenue

- Clean up.

Chapman Avenue to Elizabeth Street

- Placing Blacktop in water main trench.
- Installing a few remaining new water services
- Hooking the water main into side street mains
- Clean up.

Elizabeth Street to Lincoln Street

- Resuming Installing new 12" water main to Lincoln Street

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Thursday 09/25/14

Metcalfe Drive to Chapman Avenue

- Clean up.

Chapman Avenue to Elizabeth Street

- Placing Blacktop in water main trench.
- Installing a few remaining new water services
- Hooking the water main into side street mains
- Clean up.

Elizabeth Street to Lincoln Street

- Installing new 12" water main for the final Segment of work.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Friday 09/26/14

Metcalf Drive to Chapman Avenue

- Clean up.

Chapman Avenue to Elizabeth Street

- Placing Blacktop in water main trench.
- Installing a few remaining new water services
- Hooking the water main into side street mains
- Clean up.

Elizabeth Street to Lincoln Street

- Installing new 12" water main for the final Segment of work.

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)

The logo for C&S Companies is a dark blue square. Inside the square, the letters "C&S" are written in a large, white, stylized font. Below "C&S", the word "COMPANIES" is written in a smaller, white, sans-serif font. A registered trademark symbol (®) is located to the right of the word "COMPANIES".

Keep up to date with construction progress online at:
www.AuburnNY.gov/SouthStreet
daily schedule

[home](#)

[Monday](#) | [Tuesday](#) | [Wednesday](#) | [Thursday](#) | [Friday](#) | [Saturday](#) | [Sunday](#)

Saturday 09/27/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet

daily schedule

[home](#)

[Monday](#)

[Tuesday](#)

[Wednesday](#)

[Thursday](#)

[Friday](#)

[Saturday](#)

[Sunday](#)

Sunday 09/28/14

Metcalfe Drive to Chapman Avenue

- Contractor not working.

Chapman Avenue to Elizabeth Street

- Contractor not working.

Elizabeth Street to Lincoln Street

- Contractor not working

This work schedule is contingent upon the weather conditions and unforeseen construction problems. If you feel that construction operations have severely impacted your area without proper notification contact our office immediately. Unexpected water, power or communication interruptions may occur. Every effort will be made to repair such interruptions as soon as possible. We appreciate your patience and apologize for any inconvenience.



[welcome](#)

[where are we now?](#)

[daily schedule](#)

[map](#)

[contacts](#)

[give'em a brake](#)



Keep up to date with construction progress online at:

www.AuburnNY.gov/SouthStreet
